



INNAMINCKA
PETROLEUM
ACN 101 313 777

Office 1 - Ground Floor
924 Gympie Road
CHERMSIDE QLD 4032

PO Box 2378
CHERMSIDE QLD 4032
Telephone: (07) 3359 8988
Facsimile: (07) 3359 8985
www.innapet.com.au

ANNOUNCEMENT TO ASX

Date: 4 April 08

To: Australian Securities Exchange
Companies Announcement Office
Electronic Lodgment System

Dear Sir

Drilling Report - Flax 7

Innamincka Petroleum advises that as of 06:00 hours this morning, the Flax 7 development well was at a depth of 1401 m and drilling ahead. Surface casing has been set to a depth of 882 m.

The well is prognosed to reach a total depth of 2830 metres over an operational period of 22 days.

Daily updates of drilling progress are posted also on the company website www.innapet.com.au

Participants in the project are:

Innamincka (operator)	75%
SCGAU	25%

Yours sincerely

Innamincka Petroleum Limited

Leni Stanley
Company Secretary




FLAX 7 TIME DEPTH CURVE ACTUAL VS PROGNOSED

WELL DETAILS	
Rig:	Ensign Rig 30
RT:	96.0 m
GL:	88.9 m
Total Depth:	2830 m (Planned)
Drill Days:	22 from spud

HOLE / CASING SIZES	
311 mm (12-1/4")	Surface hole to 885m
245 mm (9-5/8")	Surface Casing Set @ 882 m
216 mm (8-1/2")	Main Hole to XXXX m (TD)
178 mm (7")	Production Casing Set @ XXXX m

LOCATION DETAILS	
Well Type:	Development
Permit:	PRL 14
Distance:	120 km NNE of Moomba

MAJOR DATES	
Well Spudded:	06:00 hrs 31 Mar 08
Reached TD:	XX:XX hrs XX Apr 08
Rig Released:	XX:XX hrs XX Apr 08

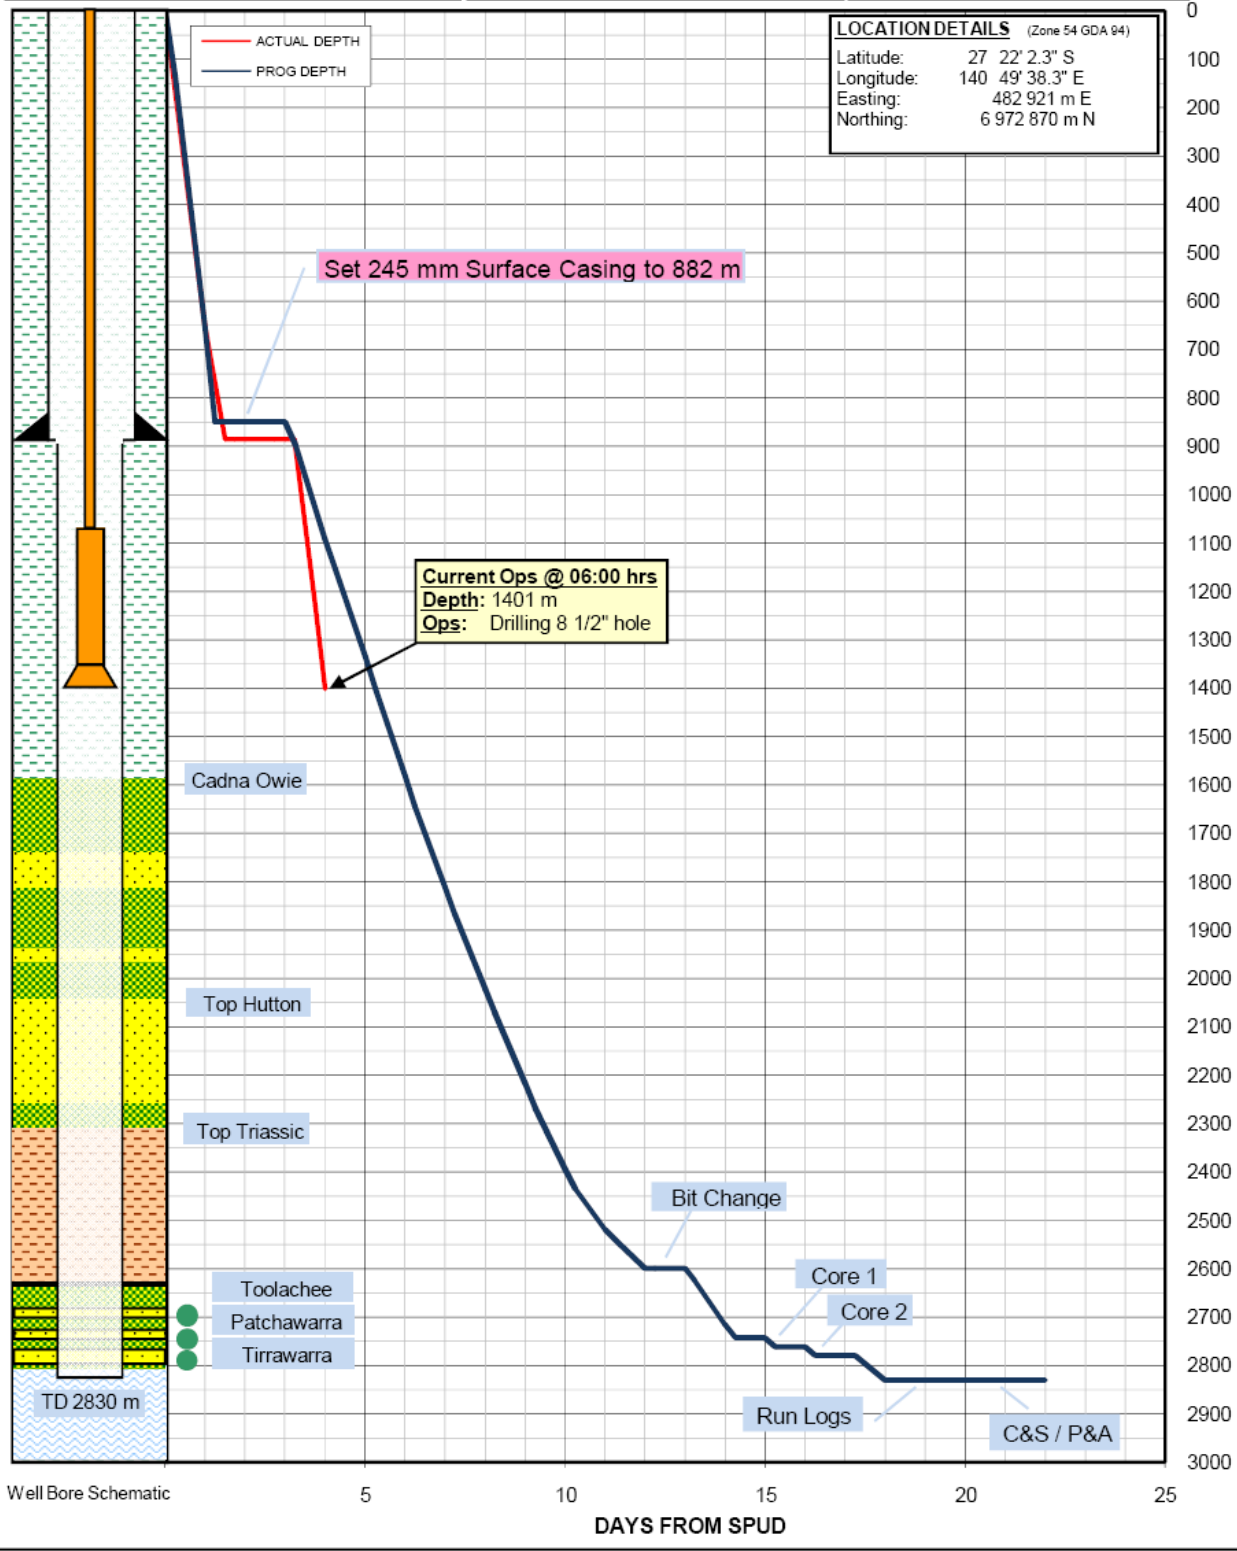

Well Bore Schematic

5 10 15 20 25

DAYS FROM SPUD
